




**PROJECT INFORMATION**

Project Name	<b>ASHBURN ROAD SIDEWALK</b>
Project Description	This project provides funding to design and construct a sidewalk along the eastern side of Ashburn Road between Partlow Road and the W&OD Trail.
Project Type	Sidewalks & Trails
Project Phase Funding	Design Phase, Construction Phase
Program Department Contact	Jim Zeller, DTCI 571.258.3548 James.Zeller@loudoun.gov
DTCI Contact	Kent Marris, DTCI 571.258.3182 Kent.Marris@loudoun.gov
Election District	Ashburn, Broad Run
Supervisor	Turner, Glass

**PROJECT BUDGET & SCHEDULE**

<b>Budget</b>	
Design	\$43,689
Construction	\$1,015,320
FFE	\$0
Land	\$178,991
Proffered Land	\$0
<b>Total Project Cost:</b>	<b>\$1,238,000</b>
<b>Project Phase Progress:</b>	
Land, Easement, ROW Phase 100%	100%
Design Phase 100%	100%
Construction Phase 100%	100%
FFE Phase	N/A
<b>Construction Phase Completion:</b>	<b>Summer 2020</b>
<b>Project Revenue(s)</b>	
Local Tax Funding	\$1,238,000
Sidewalk Contingency	\$0
<b>Total Revenue</b>	<b>\$1,238,000</b>

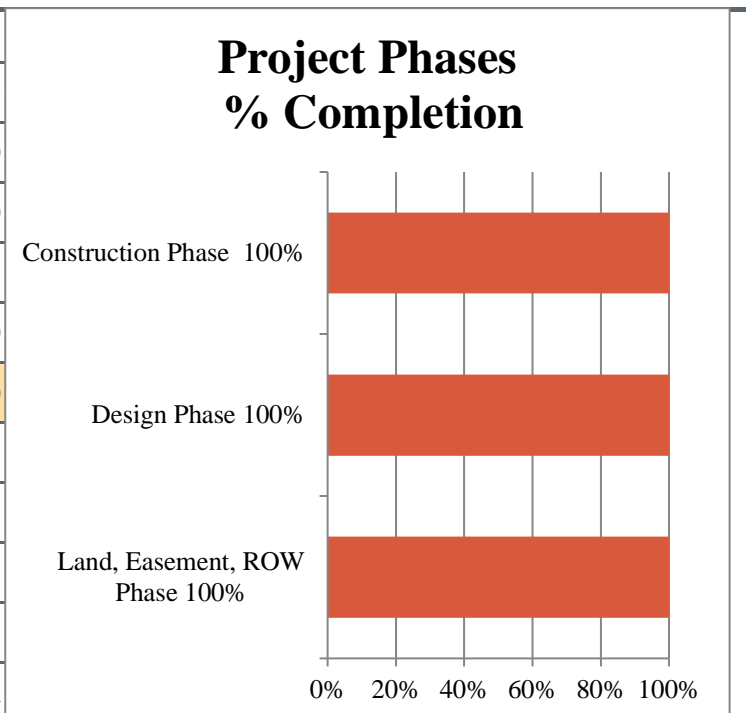

**Project Status Update:**

In this quarter, the contractor completed the initial scope of work and the project is considered substantially complete. In the next quarter, the contractor and DTCI will work on addressing punch list items and obtaining street acceptance from VDOT.
